

# Insert Solid Fuel Burning Appliance Installation Inspection Checklist




<b>Date</b>	
<b>Owners Name</b>	
<b>Building Consent Number</b>	
<b>Site Address</b>	
<b>Installers Name</b>	
<b>Supervisors Name</b>	

	Comments
Make and Model (as per approved documents)	
Appliance has been tested to appendix E of AS/NZS 2918:2001	
Register has been sealed	
Chimney has been cleaned and swept	
Chimney Structure is sound (both Internal and External)	
Venting requirements been met	
Hearth compliant with manufacturers information (Type, Dimension and Thickness)	
Seismic restraints fitted (Type/gauge)	
Mantel clearance have been achieved	
Flue system as specified in approved documents	
Flue fixed to spigot	
Flue fixing at joins and sealed	
Flue achieves the minimum height set out as in AS/NZS 2918	
Smoke alarms tested, positioned as per NZBC F7	
Ventilated cowl has been fitted	


**Additional comments**

**Note:**

**Any changes from the approved consent documents will require an amendment or minor variation prior to any installation taking place.**

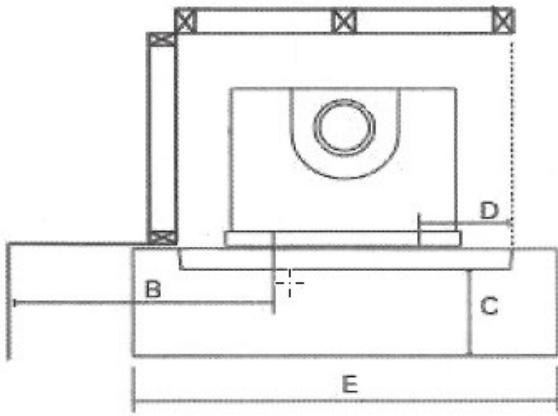

Plan Elevation

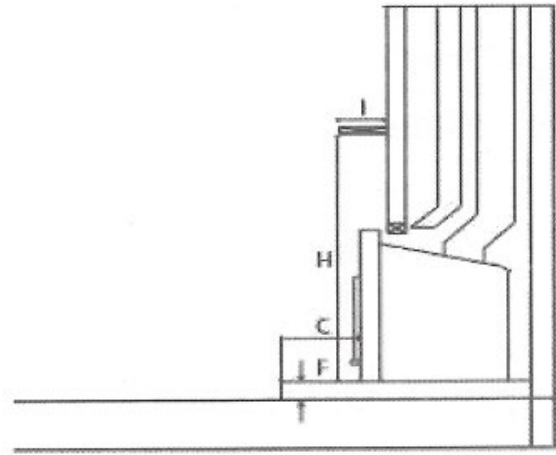

Side Elevation

<b>B</b>	
<b>C</b>	
<b>D</b>	
<b>E</b>	
<b>F</b>	
<b>H</b>	
<b>I</b>	
